GreenTech production downtime review

Findings and 90-day improvement plan

Dashboard period: 1 March to 31 August 2025

Performance snapshot

More than half of all batches exceeded planned production time

56.3%

363 of 645 batches were delayed

This delay level makes recurring downtime a production-capacity issue, not only a maintenance statistic.

21.74

days of production time lost

885

recorded downtime incidents

13

distinct downtime factors

4

maximum incidents on one batch


Priority: remove repeat non-operator causes first, then use scheduling changes and focused coaching to protect the improvement.

Source: Factor Overview. Delay rate = 363 ÷ 645


Non-operator causes dominate downtime

Non-operator causes account for 68.93% of incidents and 70.14% of lost time

Downtime incidents by source

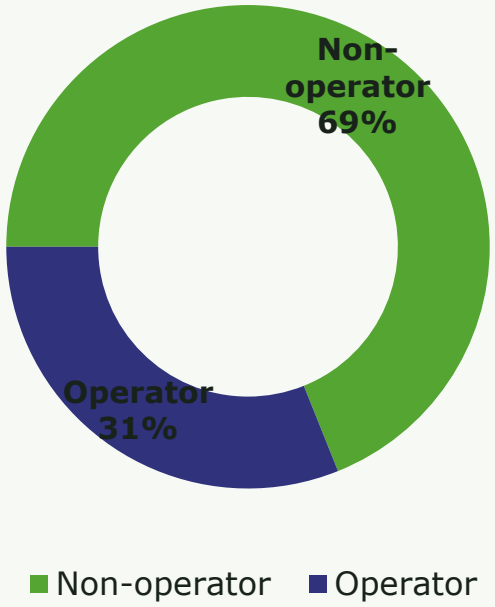

Leading downtime factors

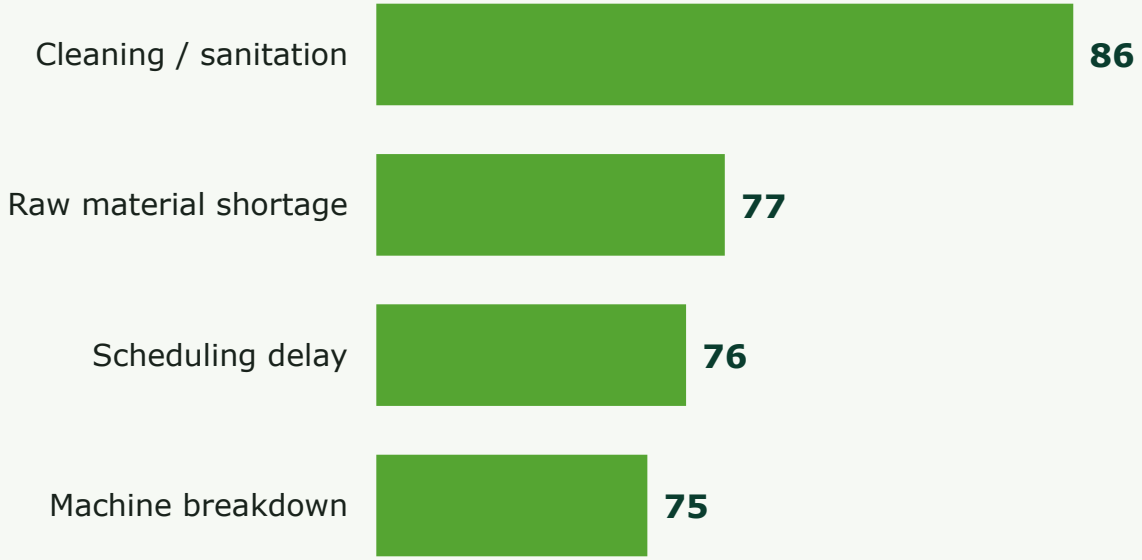


Operator mistakes recorded 67 incidents and ranked below sanitation, materials, scheduling, and machine breakdowns.

Source: Factor Overview and Duration Analysis


GreenFoam carries the largest product delay

All four products exceeded planned average production time

Total production delay by product (hours)

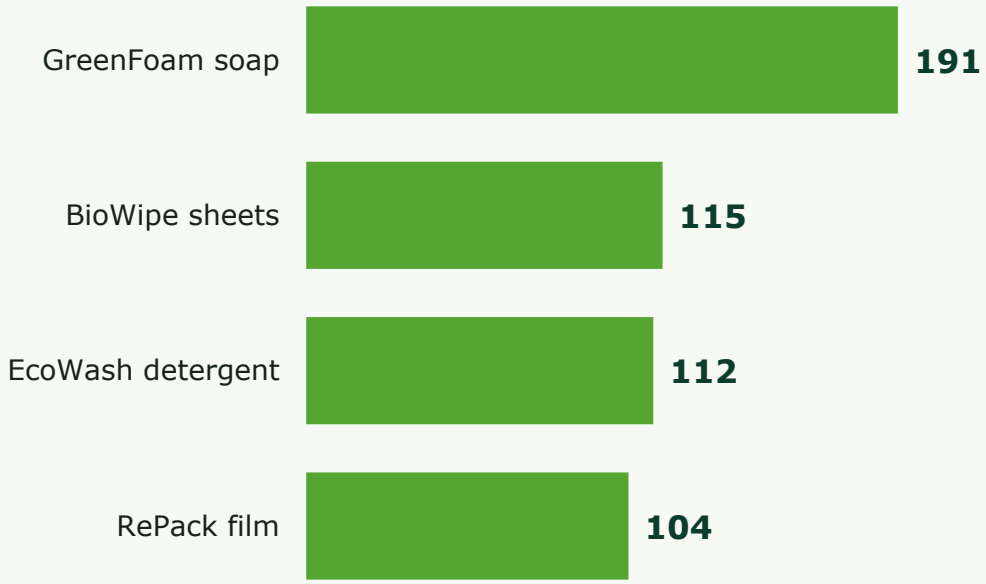

Average planned and actual duration (hours)

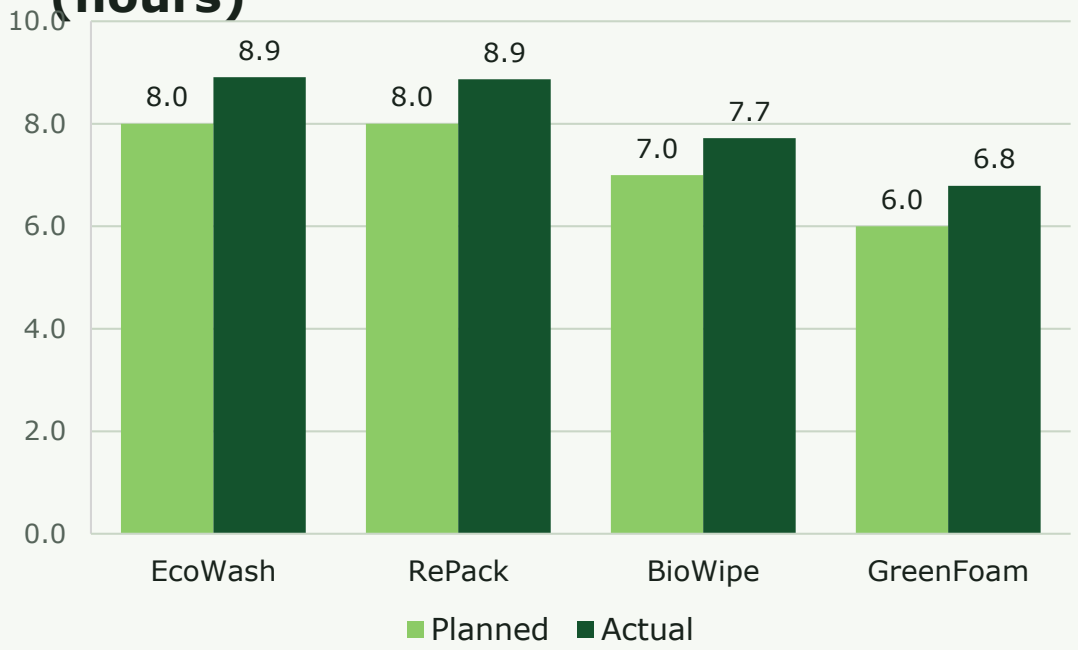


GreenFoam needs a focused root-cause sprint. Across products, actual average duration runs 0.72 to 0.91 hours above plan.

Source: Duration Analysis

Operator risk differs by volume and rate

Paul has the largest total impact, while Linda has the highest delayed-batch rate

Hours lost by operator

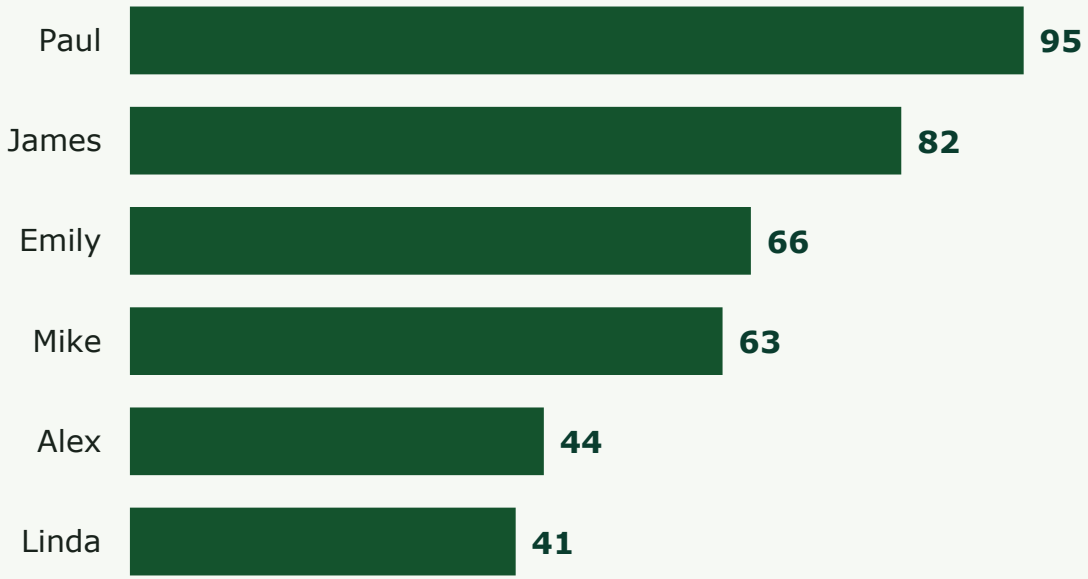

Highest delayed-batch rates




Management implication: compare delayed-batch rate with workload and hours lost before assigning training or performance actions.

Source: Factor Overview and Duration Analysis

Multi-batch scheduling pilot

Paul's filtered page shows concentrated workload and repeated downtime exposure

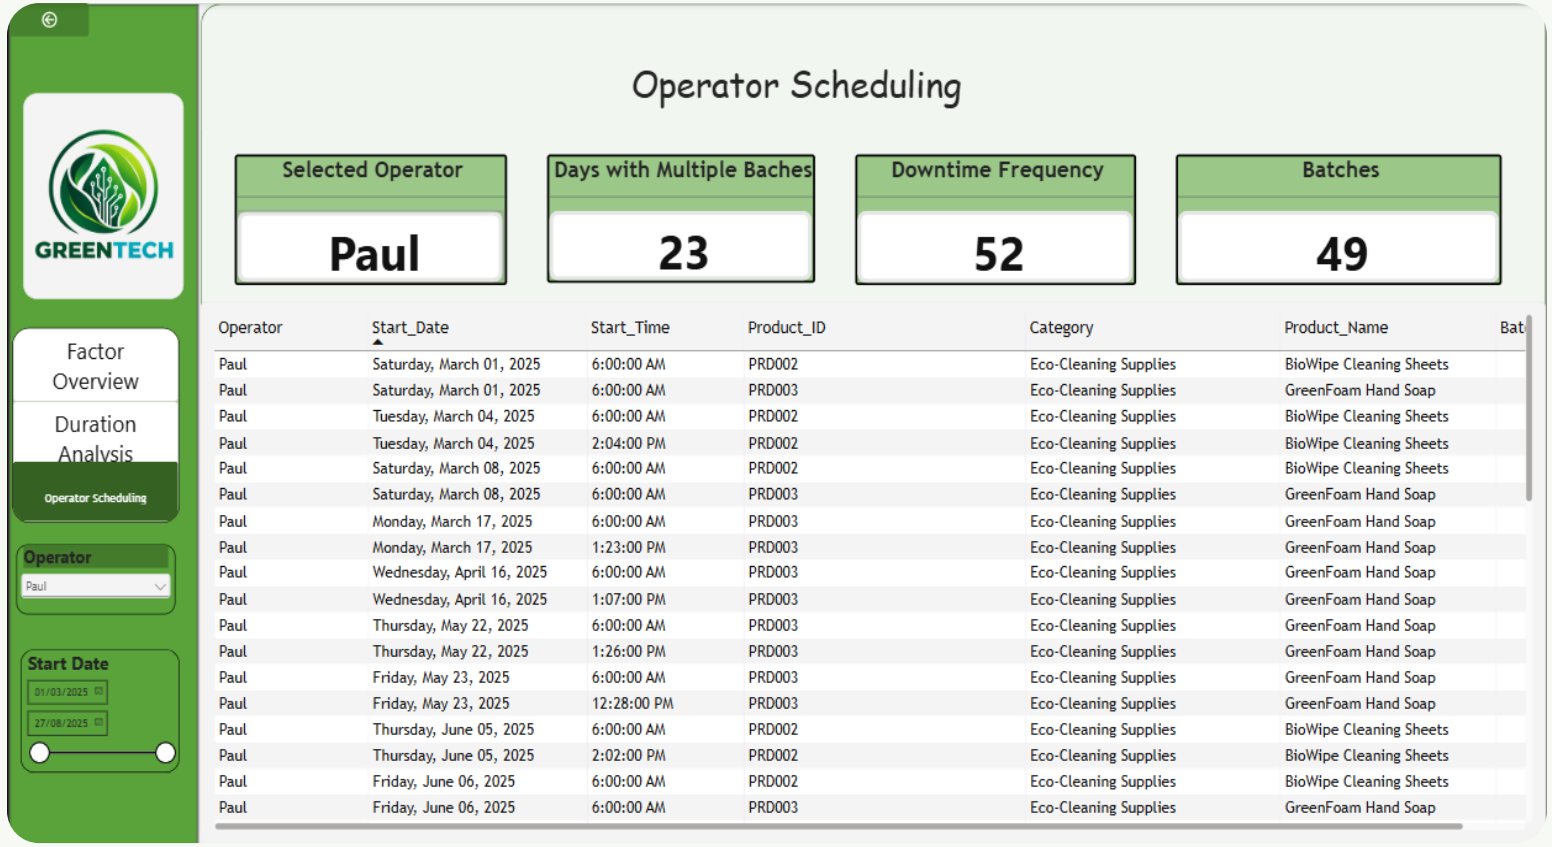

Operator	Start_Date	Start_Time	Product_ID	Category	Product_Name	Bat
Paul	Saturday, March 01, 2025	6:00:00 AM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Saturday, March 01, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Tuesday, March 04, 2025	6:00:00 AM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Tuesday, March 04, 2025	2:04:00 PM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Saturday, March 08, 2025	6:00:00 AM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Saturday, March 08, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Monday, March 17, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Monday, March 17, 2025	1:23:00 PM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Wednesday, April 16, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Wednesday, April 16, 2025	1:07:00 PM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Thursday, May 22, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Thursday, May 22, 2025	1:26:00 PM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Friday, May 23, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Friday, May 23, 2025	12:28:00 PM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	
Paul	Thursday, June 05, 2025	6:00:00 AM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Thursday, June 05, 2025	2:02:00 PM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Friday, June 06, 2025	6:00:00 AM	PRD002	Eco-Cleaning Supplies	BioWipe Cleaning Sheets	
Paul	Friday, June 06, 2025	6:00:00 AM	PRD003	Eco-Cleaning Supplies	GreenFoam Hand Soap	

23
multi-batch days

49
batches on those days

52
downtime events

Derived: 2.13 batches per multi-batch day and 1.06 downtime events per batch.

The dashboard shows association, not causation. Test a batch cap and product-sequencing rule for four weeks.

Source: Operator Scheduling, Paul, MultipleBatchPerDay = True

Five priorities address the largest losses

Each recommendation links an owner to a measurable 90-day result

Priority	Action	Owner	Proposed 90-day measure
1. Non-operator reliability	Run a weekly Pareto review for sanitation, materials, scheduling, and breakdowns. Close the top recurring cause each week.	Maintenance, Materials, QA	**Non-operator lost time below 65%**
2. GreenFoam root cause	Map every stop, changeover, and wait point for GreenFoam. Test fixes on the highest-loss step.	Line owner, Process Engineering	**Delay time at or below 162 hours**
3. Multi-batch scheduling	Pilot a daily batch cap, complexity-based sequencing, and material staging on comparable shifts.	Production Planning	**Fewer than 0.95 events per pilot batch**
4. Standard work	Use sanitation and changeover checklists plus a 10-minute readiness check before each run.	Line Leads	**15% fewer sanitation and scheduling incidents**
5. Focused coaching	Coach repeat operator-attributable events after adjusting for workload, product mix, and shift conditions.	Operations Manager	**Operator share below 27%**

Recommendations based on the dashboard findings. Targets are proposed.

90-day implementation plan

A short pilot cycle turns the dashboard into an operating routine

Days 0 to 30	Days 31 to 60	Days 61 to 90
Confirm KPI definitions and owners. Review the top factors daily. Baseline performance by product, shift, and operator.	Pilot GreenFoam countermeasures and the multi-batch sequencing rule. Start coaching for repeat operator-attributable events.	Expand fixes that reduced loss. Lock standard work. Review the scorecard weekly with named owners.

Proposed 90-day scorecard

≤50%
delayed-batch rate

≤19.6
days lost

≤162h
GreenFoam delay

≤73
top-factor incidents

Decision requested: approve the GreenFoam and multi-batch pilots, assign owners, and review progress every week.

Targets are proposed from current dashboard baselines
